


Asbestos Register

(Hazardous Materials and Risk Assessment)

School:	Jerrabomberra Public School (4633)
Region:	Southern NSW AMU
State Electorate:	Monaro
Local Government Area:	Queanbeyan-Palerang

Last Reviewed By:	WSP 11-SEP-2017
Last Revised By:	

Historical Fibro In Grounds Investigations/Events	No
<p>No previous investigations have been recorded against the school. However, asbestos containing materials maybe present in grounds from time to time and caution must be exercised prior to any grounds disturbance.</p>	

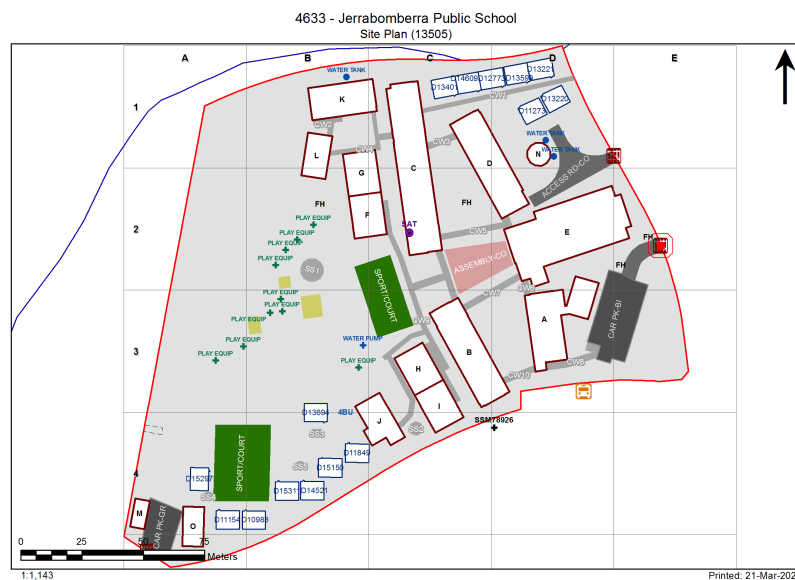

Preface to Asbestos Register

Limitations

Asbestos Registers established (first surveyed 2007/08) and maintained for the Department of Education (DoE) are limited in extent, in that:

1. All inspections and surveys of materials and finishes in DoE facilities are non-disturbance, with
2. Samples undertaken by hygienist to determine whether a sample is an Asbestos Containing Material (ACM),
3. The hygienist may apply a single sample to like materials within a space and adjoining spaces, but not normally between buildings,
4. Successive inspections have reduced any inconclusive records such as 'assumed asbestos' in difficult to access areas, by undertaking additional sampling with lifting devices.
5. In compliance with WHS Act 2011 and WHS Regulations 2017, additional inspections have been undertaken in ceiling spaces and sub-floor areas where access is possible.
 - o Where the ground floor is slab on ground, no inspection is made beneath the slab.
 - o Where fibro fragments (ACM taken for sampling) are located in ceiling spaces or sub floor voids air monitoring is normally undertaken at time of sampling, and clearance undertaken as soon as practicable.
6. No attempt has been made to identify any ACM that is hidden from view or encapsulated within
 - o Any wall cavity
 - o Sub floor area, particularly formwork for slabs in/on ground,
 - o Services (that may use ACM) such as: pipe lagging, asbestos cement pipes, flues.
7. All known ACM in Grounds (Fibro in Grounds) is made available in associated site specific asbestos management plans in DoE electronic files.
Notwithstanding information provided, ACM may be present in grounds from time to time and caution must be exercised prior to any grounds disturbance.

Use of the Asbestos Register

Prior to any disturbance works being undertaken in a building to which this asbestos register applies it will be necessary to confirm the extent of any ACM by a disturbance investigation:

- If the building was built prior to 2003
- If any ACM has been identified in the Asbestos Register for the building.

Update of Asbestos Registers

Asbestos Register Data is updated regularly by the DoE Hygienist Panel via the Online Asbestos Register Tool (Managed by Business Systems, School Infrastructure NSW). Internal users can view the latest edition of the Asbestos Register in the AMS.

Please note: The Department's external website may not contain the latest revision of the Asbestos Register.

Notes 1: Vermiculite

- During 2018/19, all vermiculite occurrences in DoE schools identified in 2007/08, were 'composite tested' in accordance with a safe work NSW agreed procedure. This required multiple testing of all vermiculite occurrences.
- During the period 2007/08 to 2018/19, some vermiculite has been over sheeted and a warning is indicated for schools where this has happened.

Note 2: DoE website link for information is here:

<https://www.schoolinfrastructure.nsw.gov.au/about-us/working-with-us/schools-asbestos-register.html>

<https://education.nsw.gov.au/about-us/strategies-and-reports/our-reports-and-reviews/schools-asbestos-register>

Note 3: Material Condition Assessment

The material condition assessment descriptors from Section 3 of the Asbestos Management Plan (AMP) is extracted below. Please read the AMP in its entirety for further information.

3.3.2.1 Material condition assessment

The OART records the material condition of identified ACM in the following format:

Rating	Description
Good condition (1)	For non-friable asbestos that is sealed and has no visible damage. This primarily related to asbestos cement (AC) sheet and vinyl tiles
Minimal damage (2)	For non-friable asbestos that has a very small amount of damage, eg hairline cracks.
Some damage / unsealed (3)	For non-friable asbestos with significant breakage or several small areas where material has been damaged, revealing loose asbestos fibres. Non-friable asbestos that is unsealed.
Poor condition (4)	For non-friable asbestos that has extensive damage. Visible asbestos debris
Friable asbestos (5)	Any occurrence of friable asbestos

Product	Material Description	Extent	Location	Material Condition	Risk Status	Remediation Priority	Result
B00A - Administration/Staff Facilities - 2002 - Brick/Veneer							
Exterior							
Underfloor Voids - Slab on Ground	No Asbestos Found						
Ceiling Voids	No Asbestos Found						
Interior							
B00A - R0003 - Main Switch Board - 2.62 m2							
No Asbestos							
B00A - R0004 - Cleaning Distributed Store - 2.38 m2							
No Asbestos							
B00A - R0007 - Interview - 13.11 m2							
Floor Coverings Res/Textile	No Asbestos Found						
B00A - R0008 - Access Shower/Toilet - 5.51 m2							
No Asbestos							
B00A - R0009 - Sick Bay - 8.33 m2							
No Asbestos							
B00A - R0010 - Clerical Office - 17.72 m2							
Floor Coverings Res/Textile	No Asbestos Found						
B00A - R0011 - Entry Vestibule - 24.38 m2							
Floor Coverings Res/Textile	No Asbestos Found						
B00A - R0014 - Security Store - 18.53 m2							
No Asbestos							
B00A - R0015 - Staff Toilet - 4.83 m2							
No Asbestos							
B00A - R0016 - Staff Toilet - 4.83 m2							
No Asbestos							
B00A - R0017 - Staff Toilet - 4.83 m2							
No Asbestos							
B00A - R0019 - External Movement - 90.79 m2							
No Asbestos							
B00A - R0020 - Staff Room - 20.63 m2							
Floor Coverings Res/Textile	No Asbestos Found						
B00A - R0023 - Clerical Office - 37.16 m2							
No Asbestos							
B00A - R0024 - Movement - 68.56 m2							
No Asbestos							
B00A - R0025 - Deputy Principal - 15.09 m2							
No Asbestos							
B00A - R0026 - Principal - 21.11 m2							
No Asbestos							
B00A - R0027 - Clerical/Printing - 19.1 m2							
No Asbestos							
B00A - R0028 - Distribution Board - .59 m2							
No Asbestos							Note: No inspection of live electrical installation
B00A - R0029 - Staff Room Annexe - 28.82 m2							
No Asbestos							
B00A - R0030 - Staff Room - 54.6 m2							
No Asbestos							
B00A - R0031 - Staff Kitchen - 10.71 m2							
No Asbestos							
B00A - R0032 - External Movement - 48.72 m2							

No Asbestos		
B00B - General Learning/Pupil Facilities - 2002 - Brick/Veneer		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00B - R0001 - External Movement - 113.26 m2		
No Asbestos		
B00B - R0002 - Practical Activities - 1hb - 19.84 m2		
No Asbestos		
B00B - R0003 - Home Base Store - 7.84 m2		
No Asbestos		
B00B - R0004 - External Movement - 2.06 m2		
No Asbestos		
B00B - R0005 - Home Base - 57.36 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00B - R0006 - Withdrawal Space - 2hb - 11.38 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00B - R0007 - Home Base - 56.75 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00B - R0008 - Practical Activities - 1hb - 20.08 m2		
No Asbestos		
B00B - R0009 - Home Base Store - 7.74 m2		
No Asbestos		
B00B - R0010 - Distribution Board - .57 m2		
		Note: No inspection of live electrical installation
No Asbestos		
B00B - R0011 - External Movement - 4.64 m2		
No Asbestos		
B00B - R0012 - Home Base Store - 7.92 m2		
No Asbestos		
B00B - R0013 - Practical Activities - 1hb - 20.04 m2		
No Asbestos		
B00B - R0014 - Home Base - 57.36 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00B - R0015 - Withdrawal Space - 2hb - 11.45 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00B - R0016 - Home Base - 57.35 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00B - R0017 - Practical Activities - 1hb - 19.62 m2		
No Asbestos		
B00B - R0018 - Home Base Store - 6.46 m2		
No Asbestos		
B00B - R0019 - Cleaning Distributed Store - 3.12 m2		
No Asbestos		
B00B - R0020 - Drinking Facilities - 10.79 m2		
No Asbestos		
B00B - R0021 - Toilets - Boys - 18.39 m2		
No Asbestos		
B00B - R0022 - Toilets - Girls - 17.78 m2		
No Asbestos		
B00B - R0023 - Kiln Room - 6.16 m2		

No Asbestos		
B00C - General Learning/Library - 2002 - Brick/Veneer		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00C - R0002 - Staff Toilet - 5.77 m2		
No Asbestos		
B00C - R0003 - Cleaning Distributed Store - 4.14 m2		
No Asbestos		
B00C - R0004 - Special Programs Store - 5.86 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0005 - Reading Area - 34.02 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0006 - Distribution Board - .54 m2		
		Note: No inspection of live electrical installation
No Asbestos		
B00C - R0007 - Communications Room - 16.86 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0010 - Laundry - Type 2 - 7.54 m2		
No Asbestos		
B00C - R0011 - Toilets - Boys/Girls - 20.02 m2		
No Asbestos		
B00C - R0012 - Home Base Store - 9.99 m2		
No Asbestos		
B00C - R0013 - Practical Activities - 1hb - 19.78 m2		
No Asbestos		
B00C - R0014 - Home Base - 57.28 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0015 - Withdrawal Space - 2hb - 11.43 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0016 - Home Base - 57.35 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0017 - External Movement - 2.37 m2		
No Asbestos		
B00C - R0018 - Home Base Store - 7.88 m2		
No Asbestos		
B00C - R0019 - Practical Activities - 1hb - 19.92 m2		
No Asbestos		
B00C - R0020 - External Movement - 184.11 m2		
No Asbestos		
B00C - R0021 - Practical Activities - 1hb - 19.76 m2		
No Asbestos		
B00C - R0022 - Home Base Store - 7.05 m2		
No Asbestos		
B00C - R0023 - Distribution Board - .55 m2		
		Note: No inspection of live electrical installation
No Asbestos		
B00C - R0024 - External Movement - 2.54 m2		
No Asbestos		
B00C - R0025 - Home Base - 57.28 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0026 - Home Base - 57.51 m2		

Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0027 - Home Base Store - 7.84 m2		
No Asbestos		
B00C - R0028 - Practical Activities - 1hb - 19.87 m2		
No Asbestos		
B00C - R0029 - Withdrawal Space - 2hb - 11.35 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00C - R0030 - Movement - 26.65 m2		
No Asbestos		
B00C - R0031 - External Movement - 6.05 m2		
No Asbestos		
B00C - R0032 - Reading Area - 185.06 m2		
No Asbestos		
B00D - General Learning/Pupil Facilities - 2003 - Brick/Veneer		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00D - R0001 - External Movement - 2.55 m2		
No Asbestos		
B00D - R0002 - Home Base Store - 7.86 m2		
No Asbestos		
B00D - R0003 - Practical Activities - 1hb - 19.77 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0004 - Home Base - 58.19 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0005 - Withdrawal Space - 2hb - 11.01 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0006 - Home Base - 58.12 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0007 - Practical Activities - 1hb - 19.93 m2		
No Asbestos		
B00D - R0008 - Home Base Store - 6.98 m2		
No Asbestos		
B00D - R0009 - Communications Cupboard - .85 m2		
No Asbestos		
B00D - R0010 - Movement - 4.63 m2		
No Asbestos		
B00D - R0011 - Distribution Board - .38 m2		
No Asbestos		Note: No inspection of live electrical installation
B00D - R0012 - Home Base Store - 7.44 m2		
No Asbestos		
B00D - R0013 - Practical Activities - 1hb - 19.95 m2		
No Asbestos		
B00D - R0014 - Home Base - 58.04 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0015 - Withdrawal Space - 2hb - 11.08 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0016 - Home Base - 58.04 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00D - R0017 - Practical Activities - 1hb - 19.9 m2		

No Asbestos		
B00D - R0018 - Home Base Store - 7.81 m2		
No Asbestos		
B00D - R0019 - Movement - 9.94 m2		
No Asbestos		
B00D - R0020 - Toilets - Boys - 18.62 m2		
No Asbestos		
B00D - R0021 - Toilets - Girls - 17.89 m2		
No Asbestos		
B00D - R0022 - Cleaning Distributed Store - 6.17 m2		
No Asbestos		
B00D - R0023 - External Movement - 114.26 m2		
No Asbestos		
B00E - Communal Facilities/Pupil Facilities - 2003 - Brick/Veneer		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00E - R0006 - P.E Store - 16.01 m2		
No Asbestos		
B00E - R0007 - Sports Store - 15.31 m2		
No Asbestos		
B00E - R0008 - Main Switch Board - 2.52 m2		
No Asbestos		
B00E - R0009 - Cleaning Distributed Store - 3.16 m2		
No Asbestos		
B00E - R0010 - Toilets - Boys - 10.01 m2		
No Asbestos		
B00E - R0011 - Access Shower/Toilet - 4.66 m2		
No Asbestos		
B00E - R0012 - Canteen Office/Store - 8.49 m2		
No Asbestos		
B00E - R0016 - Toilets - Girls - 9.8 m2		
No Asbestos		
B00E - R0017 - Communications Cupboard - 2.04 m2		
No Asbestos		
B00E - R0018 - Cleaning Supplies - 10.08 m2		
No Asbestos		
B00E - R0019 - Garden Store - 14.15 m2		
No Asbestos		
B00E - R0020 - General Assistant/Bulk Store - 13.49 m2		
No Asbestos		
B00E - R0022 - Communal/Performance Store - 25.9 m2		
No Asbestos		
B00E - R0023 - General Storeroom - 20.29 m2		
No Asbestos		
B00E - R0024 - Communal/Performance Store - 11.04 m2		
No Asbestos		
B00E - R0025 - Raised Platform - 63.87 m2		
No Asbestos		
B00E - R0026 - Ramp - 10.95 m2		

No Asbestos		
B00E - R0027 - Movement - 7.4 m2		
No Asbestos		
B00E - R0028 - Movement - 6.52 m2		
No Asbestos		
B00E - R0029 - Hall Chair Store - 12.38 m2		
No Asbestos		
B00E - R0030 - General Storeroom - 12 m2		
No Asbestos		
B00E - R0031 - P.E Store - 23.45 m2		
No Asbestos		
B00E - R0032 - Communal Space - 365.33 m2		
No Asbestos		
B00E - R0033 - Movement - 16.23 m2		
No Asbestos		
B00E - R0034 - External Movement - 35.99 m2		
No Asbestos		
B00E - R0035 - External Movement - 282.95 m2		
No Asbestos		
B00E - R0036 - General Storeroom - 12.62 m2		
No Asbestos		
B00E - R0037 - Canteen - 41.77 m2		
No Asbestos		
B00F - General Learning - 2004 - Fibre Cement Clad		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00F - R0001 - External Movement - 38.46 m2		
No Asbestos		
B00F - R0002 - Practical Activities - 1hb - 19.39 m2		
No Asbestos		
B00F - R0003 - Home Base Store - 6.01 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00F - R0004 - Home Base - 59.18 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00F - R0005 - Withdrawal Space - 2hb - 11.35 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00F - R0006 - Home Base - 59.17 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00F - R0007 - Home Base Store - 6.02 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00F - R0008 - Practical Activities - 1hb - 19.4 m2		
No Asbestos		
B00G - General Learning - 2006 - Fibre Cement Clad		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00G - R0001 - External Movement - 38.47 m2		
No Asbestos		

B00G - R0002 - Practical Activities - 1hb - 19.39 m2		
No Asbestos		
B00G - R0003 - Home Base Store - 6.02 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00G - R0004 - Home Base - 59.18 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00G - R0005 - Withdrawal Space - 2hb - 11.35 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00G - R0006 - Home Base - 59.17 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00G - R0007 - Home Base Store - 6.01 m2		
Floor Coverings Res/Textile	No Asbestos Found	
B00G - R0008 - Practical Activities - 1hb - 19.4 m2		
No Asbestos		
B00H - General Learning - 2007 - Fibre Cement Clad		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00H - R0001 - External Movement - 38.46 m2		
No Asbestos		
B00H - R0002 - Practical Activities - 1hb - 19.39 m2		
No Asbestos		
B00H - R0003 - Home Base Store - 6.01 m2		
No Asbestos		
B00H - R0004 - Home Base - 59.18 m2		
No Asbestos		
B00H - R0005 - Withdrawal Space - 2hb - 11.35 m2		
No Asbestos		
B00H - R0006 - Home Base - 59.18 m2		
No Asbestos		
B00H - R0007 - Home Base Store - 6.02 m2		
No Asbestos		
B00H - R0008 - Practical Activities - 1hb - 19.4 m2		
No Asbestos		
B00I - General Learning - 2007 - Fibre Cement Clad		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00I - R0001 - External Movement - 38.47 m2		
No Asbestos		
B00I - R0002 - Practical Activities - 1hb - 19.39 m2		
No Asbestos		
B00I - R0003 - Home Base Store - 6.02 m2		
No Asbestos		
B00I - R0004 - Home Base - 59.18 m2		
No Asbestos		
B00I - R0005 - Withdrawal Space - 2hb - 11.35 m2		
No Asbestos		

B00I - R0006 - Home Base - 59.17 m2		
No Asbestos		
B00I - R0007 - Home Base Store - 6.01 m2		
No Asbestos		
B00I - R0008 - Practical Activities - 1hb - 19.4 m2		
No Asbestos		
B00J - Music/General Learning - 2007 - Timber		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00J - R0001 - Special Programs Room - 76.09 m2		
No Asbestos		
B00J - R0002 - Interview/Office - Type 3 - 7.88 m2		
No Asbestos		
B00J - R0003 - General Storeroom - 6.09 m2		
No Asbestos		
B00J - R0004 - Communications Room - 6.09 m2		
No Asbestos		
B00J - R0005 - Staff Room - 7.88 m2		
No Asbestos		
B00J - R0006 - Other-Community Use - 76.58 m2		
No Asbestos		
B00J - R0007 - Withdrawal Space - 1hb - 22 m2		
No Asbestos		
B00J - R0008 - External Movement - 20.32 m2		
No Asbestos		
B00K - General Learning - 2011 - Fibre Cement Clad		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00K - R0001 - External Movement - 51.92 m2		
No Asbestos		
B00K - R0002 - Practical Activities - 1hb - 23.87 m2		
No Asbestos		
B00K - R0003 - Home Base - 64.26 m2		
No Asbestos		
B00K - R0004 - Home Base Store - 4.17 m2		
No Asbestos		
B00K - R0005 - Withdrawal Space - 1hb - 7.63 m2		
No Asbestos		
B00K - R0006 - Practical Activities - 1hb - 19.52 m2		
No Asbestos		
B00K - R0007 - Home Base Store - 5.67 m2		
No Asbestos		
B00K - R0008 - Home Base - 58.38 m2		
No Asbestos		
B00K - R0009 - Withdrawal Space - 2hb - 10.88 m2		
No Asbestos		
B00K - R0010 - Home Base - 58.38 m2		

No Asbestos		
B00K - R0011 - Home Base Store - 5.67 m2		
No Asbestos		
B00K - R0012 - Practical Activities - 1hb - 19.52 m2		
No Asbestos		
B00L - General Learning/Pupil Facilities - 2011 - Brick/Veneer		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00L - R0001 - External Movement - 42.41 m2		
No Asbestos		
B00L - R0002 - Toilets - Boys - 17.87 m2		
No Asbestos		
B00L - R0003 - Distribution Board - .78 m2		Note: No inspection of live electrical installation
No Asbestos		
B00L - R0004 - Toilets - Girls - 17.92 m2		
No Asbestos		
B00L - R0005 - Special Programs Store - 5.74 m2		
No Asbestos		
B00L - R0006 - Staff Toilet - 4.78 m2		
No Asbestos		
B00L - R0007 - Special Programs Room - 36.68 m2		
No Asbestos		
B00L - R0008 - Special Programs Room - 35.55 m2		
No Asbestos		
B00M - Other - 2010 - Metal Shed		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00M - R0001 - General Storeroom - 65.74 m2		
No Asbestos		
B00N - Special Purpose - 2012 - Fibre Cement Clad		
Exterior		
Underfloor Voids - Slab on Ground	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00N - R0001 - Special Programs Room - 64.51 m2		
No Asbestos		
B00O - Music - 2014 - Metal Clad		
Exterior		
Underfloor Voids	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Underfloor Voids	No Asbestos Found	
Ceiling Voids	No Asbestos Found	
Interior		
B00O - R0001 - External Movement - 17.52 m2		
No Asbestos		
B00O - R0002 - Special Programs Room - 93.71 m2		

No Asbestos	
B000 - R0003 - Special Programs Store - 19.87 m2	
No Asbestos	

Demountables**OS 602 10983 - Learning Unit - Standard With P.A.A. - Placement Date : 26-NOV-2014****Exterior**

Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos

Interior**R1- Learning space/withdrawal/entry**

Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
----------------------------	------------------	------	------------------

R2- Home Base Store

End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos

OS 602 11154 - Learning Unit - Standard With P.A.A. - Placement Date : 20-JAN-2006**Exterior**

Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos

Interior**R1- Learning space/withdrawal/entry**

Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
----------------------------	------------------	------	------------------

R2- Home Base Store

End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos

OS 602 11273 - Learning Unit - Standard With P.A.A. - Placement Date : 03-DEC-2001**Exterior**

Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos

Interior**R1- Learning space/withdrawal/entry**

Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
----------------------------	------------------	------	------------------

R2- Home Base Store

End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos

OS 602 11849 - Learning Unit - Standard With P.A.A. - Placement Date : 09-MAY-2008**Exterior**

Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos

Interior**R1- Learning space/withdrawal/entry**

Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
----------------------------	------------------	------	------------------

R2- Home Base Store

End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos

OS 602 12773 - Learning Unit - Standard With P.A.A. - Placement Date : 03-DEC-2001**Exterior**

Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos

Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos
Interior			
R1- Learning space/withdrawal/entry			
Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
R2- Home Base Store			
End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos
OS 603 13220 - Learning Unit - Standard With P.A.A. A/C - Placement Date : 06-MAY-2002			
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.			
No Asbestos Found			
OS 602 13221 - Learning Unit - Standard With P.A.A. - Placement Date : 28-DEC-2001			
No Asbestos Found			
OS 602 13401 - Learning Unit - Standard With P.A.A. - Placement Date : 21-FEB-2002			
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.			
Exterior			
Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos
Interior			
R1- Learning space/withdrawal/entry			
Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
R2- Home Base Store			
End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos
OS 602 13599 - Learning Unit - Standard With P.A.A. - Placement Date : 04-DEC-2001			
Exterior			
Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos
Interior			
R1- Learning space/withdrawal/entry			
Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
R2- Home Base Store			
End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos
OS 602 13694 - Learning Unit - Standard With P.A.A. - Placement Date : 11-NOV-2019			
No Asbestos Found			
OS 602 14521 - Learning Unit - Standard With P.A.A. - Placement Date : 01-JUN-2006			
No Asbestos Found			
OS 602 14609 - Learning Unit - Standard With P.A.A. - Placement Date : 06-FEB-2003			
Exterior			
Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos
Interior			
R1- Learning space/withdrawal/entry			
Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
R2- Home Base Store			
End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos

Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos
OS 602 15150 - Learning Unit - Standard With P.A.A. - Placement Date : 04-DEC-2001			
Exterior			
Eaves Linings	Flat AC Sheeting	11.52m2	Assumed Asbestos
Landing	Compressed AC Sheet	1.2m2	Assumed Asbestos
Step Treads	Compressed AC Sheet	1.08m2	Assumed Asbestos
Interior			
R1- Learning space/withdrawal/entry			
Ceiling Structures/Linings	Flat AC Sheeting	70m2	Assumed Asbestos
R2- Home Base Store			
End Wall Panel	Flat AC Sheeting	18m2	Assumed Asbestos
Ceiling Structures/Linings	Flat AC Sheeting	3m2	Assumed Asbestos
OS 602 15297 - Learning Unit - Standard With P.A.A. - Placement Date : 27-JAN-2016			
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.			
No Asbestos Found			
OS 603 15311 - Learning Unit - Standard With P.A.A. A/C - Placement Date : 21-NOV-2008			
Note: This refurbished demountable may have asbestos present in remnant mastic in window frames.			
No Asbestos Found			
OS 971 17854 - Shed - Container (Garden/Sports/Bulk) - Placement Date : 13-DEC-2001			
No Asbestos Found			
