

# Asbestos Register


(Hazardous Materials and Risk Assessment)

School:	Ku-ring-gai High School (8416)
Region:	Northern Sydney AMU
State Electorate:	Ku-Ring-Gai
Local Government Area:	Ku-Ring-Gai

Last Reviewed By:	Greencap 13-AUG-2014
Last Revised By:	Greencap 11-AUG-2020

Historical Fibro In Grounds Investigations/Events	<b>No</b>
<p>No previous investigations have been recorded against the school. However, asbestos containing materials maybe present in grounds from time to time and caution must be exercised prior to any grounds disturbance.</p>	

8416 - Ku-ring-gai High School  
Site Plan (11557)

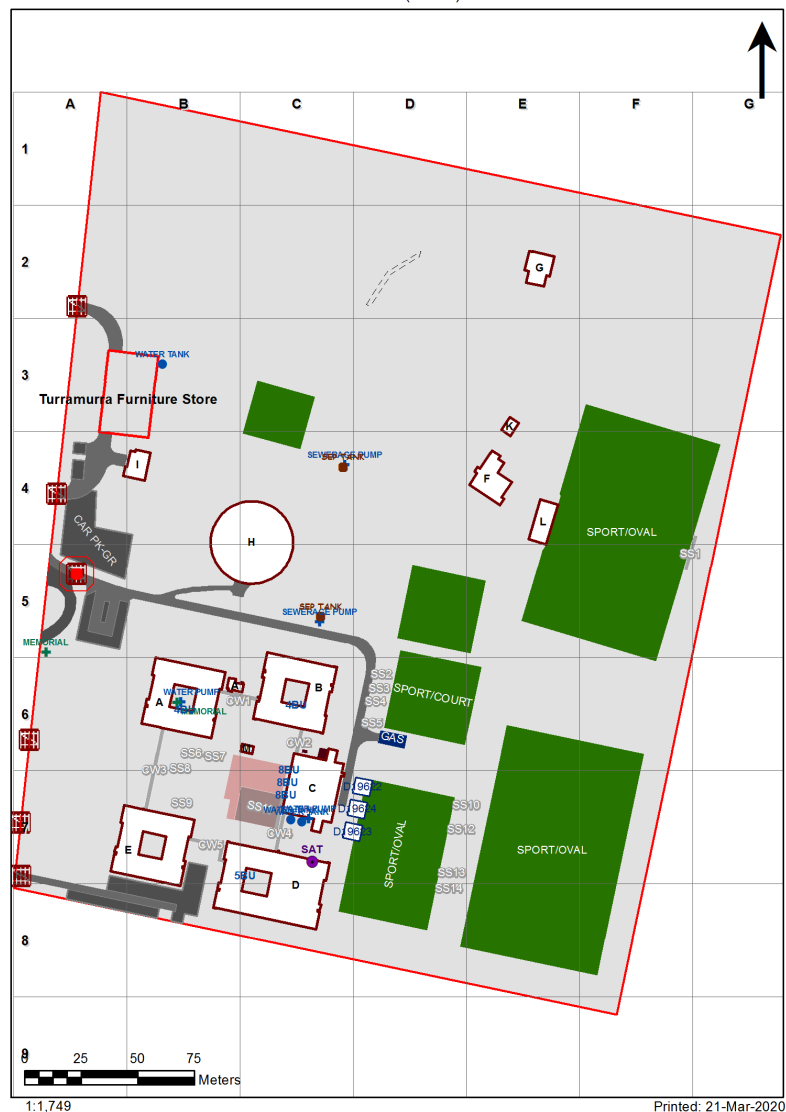

1:1,749

Printed: 21-Mar-2020

# Preface to Asbestos Register

## Limitations

Asbestos Registers established (first surveyed 2007/08) and maintained for the Department of Education (DoE) are limited in extent, in that:

1. All inspections and surveys of materials and finishes in DoE facilities are non-disturbance, with
2. Samples undertaken by hygienist to determine whether a sample is an Asbestos Containing Material (ACM),
3. The hygienist may apply a single sample to like materials within a space and adjoining spaces, but not normally between buildings,
4. Successive inspections have reduced any inconclusive records such as 'assumed asbestos' in difficult to access areas, by undertaking additional sampling with lifting devices.
5. In compliance with WHS Act 2011 and WHS Regulations 2017, additional inspections have been undertaken in ceiling spaces and sub-floor areas where access is possible.
  - o Where the ground floor is slab on ground, no inspection is made beneath the slab.
  - o Where fibro fragments (ACM taken for sampling) are located in ceiling spaces or sub floor voids air monitoring is normally undertaken at time of sampling, and clearance undertaken as soon as practicable.
6. No attempt has been made to identify any ACM that is hidden from view or encapsulated within
  - o Any wall cavity
  - o Sub floor area, particularly formwork for slabs in/on ground,
  - o Services (that may use ACM) such as: pipe lagging, asbestos cement pipes, flues.
7. All known ACM in Grounds (Fibro in Grounds) is made available in associated site specific asbestos management plans in DoE electronic files.  
Notwithstanding information provided, ACM may be present in grounds from time to time and caution must be exercised prior to any grounds disturbance.

## Use of the Asbestos Register

Prior to any disturbance works being undertaken in a building to which this asbestos register applies it will be necessary to confirm the extent of any ACM by a disturbance investigation:

- If the building was built prior to 2003
- If any ACM has been identified in the Asbestos Register for the building.

## Update of Asbestos Registers

Asbestos Register Data is updated regularly by the DoE Hygienist Panel via the Online Asbestos Register Tool (Managed by Business Systems, School Infrastructure NSW). Internal users can view the latest edition of the Asbestos Register in the AMS.

Please note: The Department's external website may not contain the latest revision of the Asbestos Register.

## Notes 1: Vermiculite

- During 2018/19, all vermiculite occurrences in DoE schools identified in 2007/08, were 'composite tested' in accordance with a safe work NSW agreed procedure. This required multiple testing of all vermiculite occurrences.
- During the period 2007/08 to 2018/19, some vermiculite has been over sheeted and a warning is indicated for schools where this has happened.

## Note 2: DoE website link for information is here:

<https://www.schoolinfrastructure.nsw.gov.au/about-us/working-with-us/schools-asbestos-register.html>  
<https://education.nsw.gov.au/about-us/strategies-and-reports/our-reports-and-reviews/schools-asbestos-register>

## Note 3: Material Condition Assessment

The material condition assessment descriptors from Section 3 of the Asbestos Management Plan (AMP) is extracted below. Please read the AMP in its entirety for further information.

### 3.3.2.1 Material condition assessment

The OART records the material condition of identified ACM in the following format:

Rating	Description
Good condition (1)	For non-friable asbestos that is sealed and has no visible damage. This primarily related to asbestos cement (AC) sheet and vinyl tiles
Minimal damage (2)	For non-friable asbestos that has a very small amount of damage, eg hairline cracks.
Some damage / unsealed (3)	For non-friable asbestos with significant breakage or several small areas where material has been damaged, revealing loose asbestos fibres. Non-friable asbestos that is unsealed.
Poor condition (4)	For non-friable asbestos that has extensive damage. Visible asbestos debris
Friable asbestos (5)	Any occurrence of friable asbestos

Product	Material Description	Extent	Location	Material Condition	Risk Status	Remediation Priority	Result
<b>B00A - Administration/General Learning/Art - 1965 - Brick/Block</b>							
<b>Exterior</b>							
Ceiling Voids	Non Accessible Area						
Underfloor Voids - Slab on Ground	No Asbestos Found						
<b>Interior</b>							
<b>B00A - R0001 - Clinic - 8.97 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00A - R0002 - Plant - .88 m2</b>							
No Asbestos							
<b>B00A - R0003 - Art Learning Space - 86.2 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00A - R0004 - Interview/Meeting - 19.13 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	20m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R0005 - Resources Store - 6.68 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R0007 - General Learning Space - 59.1 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	59m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R0008 - Plant - .88 m2</b>							
No Asbestos							
<b>B00A - R0009 - Public Reception - 59.09 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00A - R0010 - Administration - Clerical - 9.56 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00A - R0011 - Staff - Toilet - 4.57 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00A - R0012 - Staff - Toilet - 4.56 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00A - R0013 - Movement - 7.61 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00A - R0014 - Principal Office - 17.62 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00A - R0015 - General Storeroom - 2.5 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00A - R0016 - Staff - Toilet - 2.82 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						

<b>B00A - R0017 - Administration - Clerical - 52.27 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00A - R0018 - Staff Kitchen - 15.25 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00A - R0021 - Printing/Photocopying - 14.63 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00A - R0022 - External Movement - 311.2 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( > 250 m2) - ( X25 )						
Furniture / Fixtures	Flat AC Sheeting						
<b>B00A - R0023 - External Stairs - 5.61 m2</b>							
No Asbestos							
<b>B00A - R0024 - External Stairs - 5.66 m2</b>							
No Asbestos							
<b>B00A - R0025 - Pupil Entry - 17.95 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00A - R0026 - Lift - 2.1 m2</b>							
No Asbestos							
<b>B00A - R0027 - Movement - 6.5 m2</b>							
No Asbestos							
<b>B00A - R0030 - Access Student Shower/Toilet/Change - 8.18 m2</b>							
No Asbestos							
<b>B00A - R0031 - Other-Vacant - .59 m2</b>							
No Asbestos							
<b>B00A - R0032 - External Movement - 1.57 m2</b>							
No Asbestos							
<b>B00A - R0033 - Staff Study - 33.19 m2</b>							
No Asbestos							
<b>B00A - R0034 - Tea Room - 4.03 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00A - R0035 - Handwashing Facilities - .16 m2</b>							
No Asbestos							
<b>B00A - R0036 - Handwashing Facilities - .16 m2</b>							
No Asbestos							
<b>B00A - R0037 - Plant - .47 m2</b>							
No Asbestos							
<b>B00A - R0038 - Plant - .45 m2</b>							
No Asbestos							
<b>B00A - R1001 - Art Learning Space - 65.02 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	65.00m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1002 - Distribution Board Cupboard - .88 m2</b> <span style="float: right;"><b>Note: No inspection of live electrical installation</b></span>							
No Asbestos							
<b>B00A - R1003 - General Learning Space - 59.32 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	59.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)

<b>B00A - R1004 - General Learning Space - 52.8 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	52.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1005 - General Learning Space - 52.87 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	53.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1006 - Computer Learning Space - 59.25 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	60m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00A - R1007 - Distribution Board Cupboard - .9 m2</b>							
							<b>Note: No inspection of live electrical installation</b>
No Asbestos							
<b>B00A - R1008 - General Learning Space - 40.37 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	40.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1009 - Staff Study - 38.61 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	38.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1010 - Interview/Meeting - 9.65 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	9.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1011 - Staff Lounge - 61.09 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	62m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1012 - Office/Store - 8.73 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1013 - Staff Kitchen - 18.26 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	18m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1014 - Deputy Principal Office - 19.25 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	19m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1017 - General Learning Space - 38.47 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	38.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00A - R1018 - General Learning Space - 45.78 m2</b>							

Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles	45m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00A - R1019 - External Movement - 139.67 m2</b>								
No Asbestos								
<b>B00A - R1020 - External Stairs - 5.64 m2</b>								
No Asbestos								
<b>B00A - R1021 - External Stairs - 5.61 m2</b>								
No Asbestos								
<b>B00A - R1022 - Movement - 5.44 m2</b>								
No Asbestos								
<b>B00A - R1023 - External Movement - 1.53 m2</b>								
No Asbestos								
<b>B00A - R1024 - Movement - 4.99 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )							
<b>B00A - R1025 - Leading Teacher - 13.58 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles	13m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00A - R1026 - Handwashing Facilities - .16 m2</b>								
No Asbestos								
<b>B00A - R1027 - Handwashing Facilities - .17 m2</b>								
No Asbestos								
<b>B00B - Technological &amp; Applied Studies/Music/Art - 1965 - Brick/Block</b>								
<b>Exterior</b>								
Ceiling Voids	Non Accessible Area							
Underfloor Voids	No Asbestos Found							
<b>Interior</b>								
<b>B00B - R0001 - Distribution Board Cupboard - .88 m2</b>						<b>Note: No inspection of live electrical installation</b>		
No Asbestos								
<b>B00B - R0002 - Resources Store - 27.02 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
<b>B00B - R0003 - Metal Technology L.S. - 92.11 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )							
<b>B00B - R0004 - Welding Area - 10.77 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )							
Floor Coverings Res/Textile	Vinyl Tiles	8m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R0005 - Resources Store - 8.74 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles	11m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R0007 - Performance Workshop - 103.16 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )							
<b>B00B - R0008 - Resources Store - 22.37 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							

<b>B00B - R0009 - Staff - Toilet - 3.48 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00B - R0010 - Staff - Toilet - 3.33 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00B - R0011 - General Learning Space - 53.9 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00B - R0012 - Resources Store - 3.4 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00B - R0013 - Plant - .88 m2</b>							
No Asbestos							
<b>B00B - R0014 - Food Technology L.S. - 71.98 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	72.00m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00B - R0017 - Food Technology L.S. - 77.44 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00B - R0021 - External Movement - 158.68 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 120 - 250 m2) - ( X15 )						
<b>B00B - R0022 - External Stairs - 5.55 m2</b>							
No Asbestos							
<b>B00B - R0023 - External Stairs - 5.52 m2</b>							
No Asbestos							
<b>B00B - R0024 - Food/Research Space - 45.22 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00B - R0025 - Preparation - Materials - 25.67 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00B - R0026 - General Storeroom - 20.9 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00B - R0027 - General Storeroom - 3 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00B - R0028 - Handwashing Facilities - .17 m2</b>							
No Asbestos							
<b>B00B - R1001 - Distribution Board Cupboard - .88 m2</b>						<b>Note: No inspection of live electrical installation</b>	
No Asbestos							
<b>B00B - R1002 - Design/Technology L.S. - 66.97 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00B - R1003 - Resources Store - 6.32 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00B - R1004 - Resources Store - 6.14 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00B - R1007 - Wood Technology L.S. - 79.57 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	80m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)

Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )							
<b>B00B - R1009 - Materials Store - 15.65 m2</b>								
Floor Coverings Res/Textile	Vinyl Tiles	16m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
<b>B00B - R1010 - Music Learning Space - 50.68 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	50m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1011 - Music Store - 13.62 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles	13m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1012 - Distribution Board Cupboard - .88 m2</b>								
<b>Note: No inspection of live electrical installation</b>								
No Asbestos								
<b>B00B - R1013 - Music Learning Space - 59.25 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	59.00m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1014 - Practice/Seminar - 26 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles (Under Floor Covering/Carpet)	26m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1017 - KIn Space - 21.28 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles	21m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1018 - Resources Store - 10.88 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles	10m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1019 - External Movement - 139.72 m2</b>								
No Asbestos								
<b>B00B - R1020 - External Stairs - 5.8 m2</b>								
No Asbestos								
<b>B00B - R1021 - External Stairs - 5.71 m2</b>								
No Asbestos								
<b>B00B - R1022 - Handwashing Facilities - .17 m2</b>								
No Asbestos								
<b>B00B - R1023 - Project Store - Type 1 - 8.58 m2</b>								
No Asbestos								
<b>B00B - R1024 - Dust Extraction Space - 6.78 m2</b>								
No Asbestos								
<b>B00B - R1025 - General Storeroom - 4.8 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )							
Floor Coverings Res/Textile	Vinyl Tiles	5m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00B - R1026 - Dust Extraction Space - 6.76 m2</b>								



No Asbestos							
<b>B00B - R1027 - Materials Store - 19.5 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00B - R1028 - Wood Technology L.S. - 79.46 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00B - R1029 - Handwashing Facilities - .17 m2</b>							
No Asbestos							
<b>B00B - R1030 - Art Learning Space - 65.97 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	65m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00B - R1031 - Staff Study - 34.67 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	34.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00B - R1032 - Tea Room - 4.4 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00C - Pupil Facilities - 1965 - Brick/Block</b>							
<b>Exterior</b>							
Ceiling Voids	Non Accessible Area						
Underfloor Voids - Slab on Ground	No Asbestos Found						
<b>Interior</b>							
<b>B00C - R0001 - Cleaning Supplies Store - 7.39 m2</b>							
No Asbestos							
<b>B00C - R0006 - Staff - Toilet - 2.84 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00C - R0007 - Office/Store - 12.54 m2</b>							
No Asbestos							
<b>B00C - R0008 - General Assistants - 20.02 m2</b>							
No Asbestos							
<b>B00C - R0009 - General Storeroom - 1.74 m2</b>							
No Asbestos							
<b>B00C - R0010 - Distribution Board Cupboard - .35 m2</b>							<b>Note: No inspection of live electrical installation</b>
No Asbestos							
<b>B00C - R0011 - Sport Equipment Store - 13.56 m2</b>							
No Asbestos							
<b>B00C - R0012 - Cleaning Store - Distributed - 1.6 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00C - R0013 - Tea Room - 5.45 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00C - R0015 - Stairs - 9.36 m2</b>							
No Asbestos							
<b>B00C - R0016 - Stairs - 9.37 m2</b>							
No Asbestos							
<b>B00C - R0017 - External Movement - 52.95 m2</b>							

No Asbestos							
<b>B00C - R0018 - Student Canteen - 62.52 m2</b>							
No Asbestos							
<b>B00C - R0019 - Movement - 11.04 m2</b>							
No Asbestos							
<b>B00C - R0020 - External Movement - 1.53 m2</b>							
No Asbestos							
<b>B00C - R0021 - Covered Area - 318.16 m2</b>							
No Asbestos							
<b>B00C - R0022 - Movement - 12.82 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00C - R0023 - Movement - 19.5 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00C - R0024 - Movement - 13 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00C - R0025 - External Movement - 4.36 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00C - R1001 - Cleaning Store - Distributed - 7.24 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Floor Coverings Res/Textile	Vinyl Tiles - Adhesive						
<b>B00C - R1002 - Toilets-Boys - 36.8 m2</b>							
No Asbestos							
<b>B00C - R1003 - Change - 38.48 m2</b>							
No Asbestos							
<b>B00C - R1004 - Movement - 8.85 m2</b>							
No Asbestos							
<b>B00C - R1005 - General Storeroom - 7.45 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	7m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Floor Coverings Res/Textile	Vinyl Tiles - Adhesive						
<b>B00C - R1006 - Toilets-Girls - 36.8 m2</b>							
No Asbestos							
<b>B00C - R1007 - Change - 39.06 m2</b>							
No Asbestos							
<b>B00C - R1008 - Movement - 8.92 m2</b>							
No Asbestos							
<b>B00C - R1009 - Stairs - 13.84 m2</b>							
No Asbestos							
<b>B00C - R1010 - Stairs - 13.94 m2</b>							
No Asbestos							
<b>B00D - Library/Computer Learning/Science Learning - 1965 - Brick/Block</b>							
<b>Exterior</b>							
External Wall Structure	Compressed AC Sheet	20	East facing, West facing	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos) , Amosite (brown asbestos)
Ceiling Voids	Non Accessible Area						
Underfloor Voids	No Asbestos Found						
<b>Interior</b>							

<b>B00D - R0002 - Librarian - 9.6 m2</b>							
No Asbestos							
<b>B00D - R0003 - Communication Space - 15.62 m2</b>							
No Asbestos							
<b>B00D - R0004 - Office/Store - 11.4 m2</b>							
No Asbestos							
<b>B00D - R0006 - Main Area - 297.3 m2</b>							
No Asbestos							
<b>B00D - R0007 - Communication Space - 1.04 m2</b>							
Wall Linings Internal	Flat AC Sheeting	4m2	East	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R0008 - Staff - Toilet - 2.79 m2</b>							
No Asbestos							
<b>B00D - R0011 - Chemical Store - 25.89 m2</b>							
No Asbestos							
<b>B00D - R0012 - Laboratory L.S. - 92.62 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00D - R0015 - Laboratory L.S. - 86.24 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00D - R0016 - Cleaning Store - Distributed - 2.81 m2</b>							
No Asbestos							
<b>B00D - R0017 - Plant - 1.2 m2</b>							
Door - Infill	Flat AC Sheeting	2	All surfaces	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Material - Stored / Debris Material	Flat AC Sheeting	1	All surfaces	Poor Condition - Extensive Damage (4)	Medium (2)	Medium Priority (4-5)	Chrysotile (white asbestos)
<b>B00D - R0021 - General Storeroom - 18.59 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00D - R0023 - Staff Study - 25.96 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R0024 - Resources Store - 6.25 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
Floor Coverings Res/Textile	Vinyl Tiles	7m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R0025 - Careers Advisers Office - 13.47 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	15m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R0026 - Resources Store - 6.57 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R0028 - External Stairs - 6.03 m2</b>							
No Asbestos							
<b>B00D - R0029 - External Stairs - 6.71 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R0030 - Staff Study - 59.19 m2</b>							

Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R0031 - Staff Kitchen - 6.96 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
Floor Coverings Res/Textile	Vinyl Tiles	15m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R0032 - External Movement - 181.27 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00D - R0033 - Movement - 5.98 m2</b>							
No Asbestos							
<b>B00D - R0034 - External Stairs - 5.88 m2</b>							
No Asbestos							
<b>B00D - R0035 - General Learning Space - 49.45 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles						
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00D - R0036 - Handwashing Facilities - 2.1 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles	4m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R0037 - Resources Store - 13.86 m2</b>							
Floor Coverings Res/Textile	Vinyl Sheet						
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00D - R0038 - Preparation - Science - 39.23 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Sheet						
<b>B00D - R0039 - Library Administration - 42.12 m2</b>							
No Asbestos							
<b>B00D - R0040 - Tea Room - 5 m2</b>							
No Asbestos							
<b>B00D - R0041 - Seminar - Type 1 - 11.57 m2</b>							
No Asbestos							
<b>B00D - R0042 - Seminar - Type 1 - 11.3 m2</b>							
No Asbestos							
<b>B00D - R0043 - Handwashing Facilities - .16 m2</b>							
No Asbestos							
<b>B00D - R0044 - General Learning Space - 86.17 m2</b>							
Requires Inspection							
<b>B00D - R1001 - Interview/Office - Type 1 - 12.82 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1002 - Resources Store - 5.14 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R1003 - General Learning Space - 53.61 m2</b>							

Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1004 - Distribution Board Cupboard - 1.09 m2</b>						<b>Note: No inspection of live electrical installation</b>	
Door - Infill	Flat AC Sheeting	2	All surfaces	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R1005 - Staff - Toilet - 2.82 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R1006 - General Learning Space - 59.01 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1007 - General Learning Space - 52.07 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1008 - General Learning Space - 52.37 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1009 - Resources Store - 6 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R1010 - Resources Store - 6.14 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R1016 - General Storeroom - 2.79 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00D - R1017 - Distribution Board Cupboard - 1.2 m2</b>						<b>Note: No inspection of live electrical installation</b>	
Door - Infill	Flat AC Sheeting	1	All surfaces	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00D - R1018 - General Learning Space - 53.68 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1019 - Staff Study - 26.11 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1020 - Computer Learning Space - 72.82 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1021 - Computer Store - 6.11 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1022 - Resources Store - 6.16 m2</b>							

Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1023 - General Learning Space - 53.9 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1024 - General Learning Space - 53.83 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1025 - General Learning Space - 52.73 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1026 - General Learning Space - 59.02 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles						
<b>B00D - R1028 - External Stairs - 6.03 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )						
<b>B00D - R1029 - External Stairs - 5.99 m2</b>							
No Asbestos							
<b>B00D - R1030 - External Stairs - 19.29 m2</b>							
No Asbestos							
<b>B00D - R1031 - Handwashing Facilities - .16 m2</b>							
No Asbestos							
<b>B00D - R1032 - General Learning Space - 152.57 m2</b>							
Requires Inspection							
<b>B00D - R1033 - External Movement - 136.32 m2</b>							
Requires Inspection							
<b>B00D - R1034 - External Movement - 39.03 m2</b>							
Requires Inspection							
<b>B00E - General Learning/Science Learning - 1965 - Brick/Block</b>							
<b>Exterior</b>							
External Wall Structure	Compressed AC Sheet	20	East facing, West facing	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos), Amosite (brown asbestos)
Ceiling Voids	Non Accessible Area						
Underfloor Voids - Slab on Ground	No Asbestos Found						
<b>Interior</b>							
<b>B00E - R0001 - General Learning Space - 65.34 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00E - R0002 - Plant - .89 m2</b>							
No Asbestos							
<b>B00E - R0003 - Laboratory L.S. - 98.09 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )	100.00m2	Throughout	Good Condition (1)	Medium (2)	Low Priority (2-3)	

Floor Coverings Res/Textile	Vinyl Tiles	100.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	
<b>B00E - R0006 - Laboratory L.S. - 84.64 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	87m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00E - R0007 - Plant - .91 m2</b>							
No Asbestos							
<b>B00E - R0008 - Laboratory L.S. - 79.82 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
<b>B00E - R0009 - Resources Store - 24.26 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00E - R0010 - Apparatus Storage - 8.24 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00E - R0011 - Resources Store - 11.11 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles						
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00E - R0012 - Deputy Principal Office - 15.06 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00E - R0013 - Toilets-Disabled - 4.81 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00E - R0014 - Cleaning Store - Distributed - 3.41 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00E - R0015 - Plant - 4.83 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00E - R0016 - Staff - Toilet - 4.73 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00E - R0017 - Toilets-Girls - 35.91 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
Partition Walls (Cubicles)	Flat AC Sheeting	36m2	All surfaces	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos) , Amosite (brown asbestos)
<b>B00E - R0018 - Toilets-Boys - 28.86 m2</b>							
Partition Walls (Cubicles)	Flat AC Sheeting	29m2	All surfaces	Some Damage - Unsealed (3)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos) , Amosite (brown asbestos)
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )						
<b>B00E - R0019 - Plant - 4.83 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00E - R0020 - General Learning Space - 59.4 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00E - R0021 - External Movement - 159.27 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 120 - 250 m2) - ( X15 )						
<b>B00E - R0022 - External Stairs - 5.51 m2</b>							

Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )							
<b>B00E - R0023 - External Stairs - 5.51 m2</b>								
No Asbestos								
<b>B00E - R0024 - Preparation - Science - 39.16 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
<b>B00E - R0025 - Handwashing Facilities - .16 m2</b>								
No Asbestos								
<b>B00E - R0026 - Handwashing Facilities - .16 m2</b>								
No Asbestos								
<b>B00E - R1001 - General Learning Space - 65.58 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles	65m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00E - R1002 - Distribution Board Cupboard - .91 m2</b> <span style="float: right;"><b>Note: No inspection of live electrical installation</b></span>								
No Asbestos								
<b>B00E - R1003 - Computer Learning Space - 59.47 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles	59.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00E - R1004 - General Learning Space - 53.02 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles	53.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00E - R1005 - General Learning Space - 52.87 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles	52.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00E - R1006 - General Learning Space - 59.39 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
Floor Coverings Res/Textile	Vinyl Tiles	59.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00E - R1007 - Distribution Board Cupboard - .88 m2</b> <span style="float: right;"><b>Note: No inspection of live electrical installation</b></span>								
No Asbestos								
<b>B00E - R1009 - Resources Store - 5.21 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (< 10 m2) - ( X2 )							
Floor Coverings Res/Textile	Vinyl Tiles							
<b>B00E - R1010 - Resources Store - 13 m2</b>								
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 10 - 40 m2) - ( X3 )							
Floor Coverings Res/Textile	Vinyl Tiles	14m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
<b>B00E - R1011 - General Learning Space - 59.41 m2</b>								
Floor Coverings Res/Textile	Vinyl Tiles	59.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)	
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )							
<b>B00E - R1012 - Movement Studio - 106.04 m2</b>								



Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 70 - 120 m2) - ( X8 )						
Floor Coverings Res/Textile	Vinyl Tiles	105.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00E - R1013 - General Learning Space - 59.25 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
Floor Coverings Res/Textile	Vinyl Tiles	58.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00E - R1014 - External Movement - 146.93 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 120 - 250 m2) - ( X15 )						
<b>B00E - R1015 - External Stairs - 5.69 m2</b>							
No Asbestos							
<b>B00E - R1016 - External Stairs - 5.67 m2</b>							
No Asbestos							
<b>B00E - R1017 - Handwashing Facilities - .16 m2</b>							
No Asbestos							
<b>B00E - R1018 - Handwashing Facilities - .16 m2</b>							
No Asbestos							
<b>B00E - R1019 - Staff Study - 50.15 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	50.00m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( 40 - 70 m2) - ( X5 )						
<b>B00E - R1020 - Tea Room - 3.54 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - ( < 10 m2) - ( X2 )						
<b>B00F - Art - 1925 - Brick/Block</b>							
<b>Exterior</b>							
Eaves Linings	Flat AC Sheeting	20m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Underfloor Voids	No Asbestos Found						
Ceiling Voids	Non Accessible Area						
<b>Interior</b>							
<b>B00F - R0001 - Toilets-Girls - 4.04 m2</b>							
No Asbestos							
<b>B00F - R0002 - Materials Store - 10.18 m2</b>							
No Asbestos							
<b>B00F - R0003 - Cleaning Store - Distributed - 2.96 m2</b>							
No Asbestos							
<b>B00F - R0004 - Photographic Studio - 21.69 m2</b>							
No Asbestos							
<b>B00F - R0005 - Dark Room - 22.3 m2</b>							
No Asbestos							
<b>B00F - R0007 - Workshop - 32.95 m2</b>							
No Asbestos							
<b>B00F - R0009 - External Movement - 3.52 m2</b>							
Ceiling Structures/Linings	Flat AC Sheeting	3m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00F - R0010 - External Movement - 12.34 m2</b>							
No Asbestos							
<b>B00F - R0011 - Covered Area - 42.75 m2</b>							
No Asbestos							

<b>B00F - R0012 - Movement - 2.64 m2</b>							
No Asbestos							
<b>B00F - R0013 - General Storeroom - 14.2 m2</b>							
No Asbestos							
<b>B00F - R0014 - Resources Store - 4.42 m2</b>							
No Asbestos							
<b>B00F - R0015 - Handwashing Facilities - 4.42 m2</b>							
No Asbestos							
<b>B00F - R0016 - Movement - 4.15 m2</b>							
No Asbestos							
<b>B00F - R0017 - Darkroom Space - 1.04 m2</b>							
No Asbestos							
<b>B00F - R0018 - Movement - 7.2 m2</b>							
No Asbestos							
<b>B00F - R0019 - Resources Store - .53 m2</b>							
No Asbestos							
<b>B00F - R0020 - External Movement - .94 m2</b>							
No Asbestos							
<b>B00G - Performance Learning - 1925 - Brick/Veneer</b>							
<b>Exterior</b>							
Ceiling Voids	No Asbestos Found						
Underfloor Voids	AC Fragments/Debris	2	East	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>Interior</b>							
<b>B00G - R0001 - External Movement - 6.86 m2</b>							
No Asbestos							
<b>B00G - R0002 - Performance Workshop - 70.08 m2</b>							
No Asbestos							
<b>B00G - R0003 - General Storeroom - 12.61 m2</b>							
No Asbestos							
<b>B00G - R0004 - General Storeroom - 5.21 m2</b>							
No Asbestos							
<b>B00G - R0005 - Performance Workspace - 40.14 m2</b>							
No Asbestos							
<b>B00H - Multi Purpose Facilities - 1971 - Concrete</b>							
<b>Exterior</b>							
Eaves Linings	Flat AC Sheeting	40m2	Throughout	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Underfloor Voids	No Asbestos Found						
Ceiling Voids	No Asbestos Found						
<b>Interior</b>							
<b>B00H - M0001 - Control Room - 21.31 m2</b>							
No Asbestos							
<b>B00H - R0002 - Chair Store - 14.34 m2</b>							
No Asbestos							
<b>B00H - R0004 - General Storeroom - 10.07 m2</b>							
Ceiling Structures/Linings	Flat AC Sheeting	10m2	All surfaces	Friable Asbestos (5)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos), Amosite (brown asbestos)
<b>B00H - R0005 - Staff Kitchen - 19.07 m2</b>							
Floor Coverings Res/Textile	Vinyl Tiles	20m2	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00H - R0006 - Control Room - 29.29 m2</b>							

No Asbestos							
<b>B00H - R0007 - Sport Equipment Store - 53.11 m2</b>							
No Asbestos							
<b>B00H - R0008 - General Storeroom - 9.73 m2</b>							
No Asbestos							
<b>B00H - R0009 - Cleaning Store - Distributed - 2.49 m2</b>							
No Asbestos							
<b>B00H - R0010 - Chair Store - 40.91 m2</b>							
No Asbestos							
<b>B00H - R0011 - Distribution Board Cupboard - 1.45 m2</b>						<b>Note: No inspection of live electrical installation</b>	
No Asbestos							
<b>B00H - R0013 - Movement - 2.02 m2</b>							
No Asbestos							
<b>B00H - R0014 - Stage - 70.74 m2</b>							
No Asbestos							
<b>B00H - R0015 - Movement - 1.96 m2</b>							
No Asbestos							
<b>B00H - R0017 - Multi-Purpose Space - 580.95 m2</b>							
Ceiling Structures/Linings	Vermiculite - Composite Sample - (> 250 m2) - ( X25 )						
<b>B00H - R0018 - External Movement - 15.89 m2</b>							
No Asbestos							
<b>B00H - R0019 - External Movement - 14.35 m2</b>							
No Asbestos							
<b>B00H - R0020 - External Movement - 9.17 m2</b>							
No Asbestos							
<b>B00H - R0021 - External Movement - 8.89 m2</b>							
No Asbestos							
<b>B00H - R0022 - Toilet - Lobby - 1.92 m2</b>							
No Asbestos							
<b>B00H - R0023 - Change - 27.75 m2</b>							
No Asbestos							
<b>B00H - R0024 - Toilet - Lobby - 1.8 m2</b>							
No Asbestos							
<b>B00H - R0025 - Change - 28.65 m2</b>							
No Asbestos							
<b>B00H - R0026 - Toilet - Lobby - 3.2 m2</b>							
Plant / Equipment - Air Conditioning Unit	Textile	3	Central	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00H - R0027 - Toilets-Boys - 9.37 m2</b>							
No Asbestos							
<b>B00H - R0028 - Toilet - Lobby - 2.66 m2</b>							
No Asbestos							
<b>B00H - R0029 - Toilets-Girls - 9.52 m2</b>							
No Asbestos							
<b>B00I - Student Services/Other-D.E.C. Admin - 1952 - Brick/Block</b>							
<b>Exterior</b>							
External Wall Structure - Awnings	Flat AC Sheeting	20	All surfaces	Good Condition (1)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Eaves Linings	Flat AC Sheeting	35m2	Throughout	Minimal Damage (2)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
Ceiling Voids	No Asbestos Found						

Underfloor Voids	No Asbestos Found						
<b>Interior</b>							
<b>B00I - R0001 - Uniform Shop - 18.94 m2</b>							
No Asbestos							
<b>B00I - R0002 - Uniform Shop - 10.61 m2</b>							
No Asbestos							
<b>B00I - R0004 - External Movement - 16.37 m2</b>							
Reinspect / Delete	Flat AC Sheeting	15	All surfaces	Minimal Damage (2)	Low (1)	Low Priority (2-3)	Chrysotile (white asbestos)
<b>B00I - R0005 - Other - D.E.T. Admin - 15.55 m2</b>							
No Asbestos							
<b>B00I - R0006 - Other - D.E.T. Admin - 2.14 m2</b>							
No Asbestos							
<b>B00I - R0007 - Other - D.E.T. Admin - 3.66 m2</b>							
No Asbestos							
<b>B00I - R0008 - Other - D.E.T. Admin - 11.03 m2</b>							
No Asbestos							
<b>B00I - R0009 - Movement - 4.13 m2</b>							
No Asbestos							
<b>B00I - R0010 - Uniform Shop - 12.47 m2</b>							
No Asbestos							
<b>B00K - Storage - 2011 - Brick/Block</b>							
<b>Exterior</b>							
Ceiling Voids	No Asbestos Found						
Underfloor Voids	No Asbestos Found						
<b>Interior</b>							
<b>B00K - R0001 - Machine Storage - 29.76 m2</b>							
No Asbestos							
<b>B00L - Other - 2012 - Brick/Veneer</b>							
<b>Exterior</b>							
Ceiling Voids	No Asbestos Found						
Underfloor Voids	No Asbestos Found						
<b>Interior</b>							
<b>B00L - R0001 - Other - 64.16 m2</b>							
No Asbestos							
<b>B00L - R0002 - External Movement - 40.59 m2</b>							
No Asbestos							
<b>B00L - R0003 - External Movement - 32.72 m2</b>							
No Asbestos							
<b>B00M - Building Services - 1964 - Concrete</b>							
<b>Exterior</b>							
Ceiling Voids	No Asbestos Found						
Underfloor Voids - Slab on Ground	No Asbestos Found						
<b>Interior</b>							
<b>B00M - R0001 - Cleaning Store - Distributed - 7.59 m2</b>							
No Asbestos							
<b>B00M - R0002 - Main Switchroom - 5.11 m2</b>							
No Asbestos							

## Demountables

### OS 600 19622 - Learning Unit - Small - Placement Date : 14-MAY-2019

**Note:** This refurbished demountable may have asbestos present in remnant mastic in window frames.

No Asbestos Found

### OS 600 19623 - Learning Unit - Small - Placement Date : 14-MAY-2019

**Note:** This refurbished demountable may have asbestos present in remnant mastic in window frames.

No Asbestos Found

### OS 600 19624 - Learning Unit - Small - Placement Date : 14-MAY-2019

**Note:** This refurbished demountable may have asbestos present in remnant mastic in window frames.

No Asbestos Found
